

Wastewater Upgrades





The first Concrete Pour

- 1. The concrete pour started at 2:00am 7/26/22 with 10 yards of concrete in each truck we poured 5300 total yards of concrete flooring, with 530 trucks. The last pour was done at 10:09 am on 7/26/2022.
- 2. All of the 7 day break test that we have ran have all passed the design strength test and have had all test higher than 81% design strength.

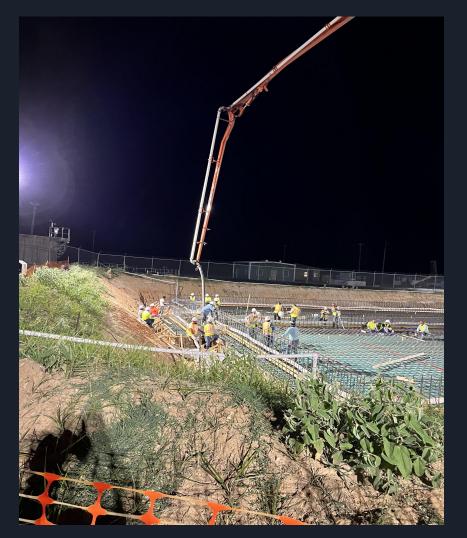

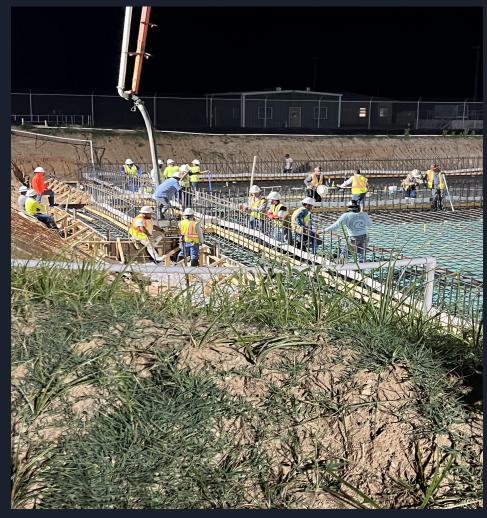

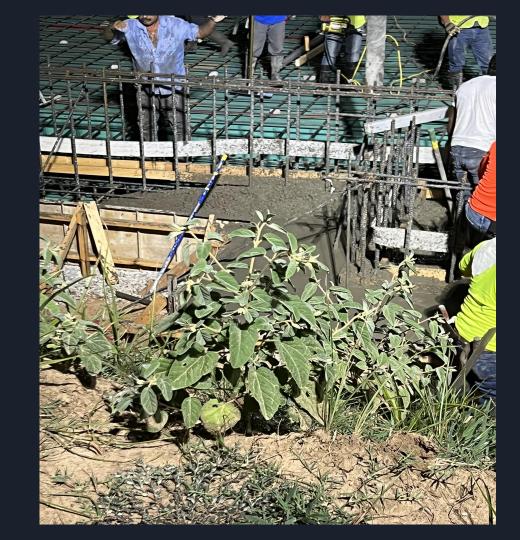

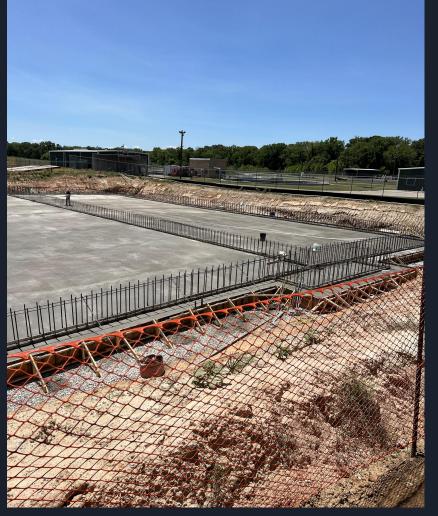



The next concrete pour

Graycon construction poured one panel of the basin back section walls. They started the pour on 8/5/2022. They are continuing to work on the pour this week.



